
Shipping a release: who does what, and when

Shows a team the 14-day path from scope freeze to full rollout, the gates and the critical chain.

STATUS	VERSION	DATE
exploration	**v1.0**	**2026-10-29**

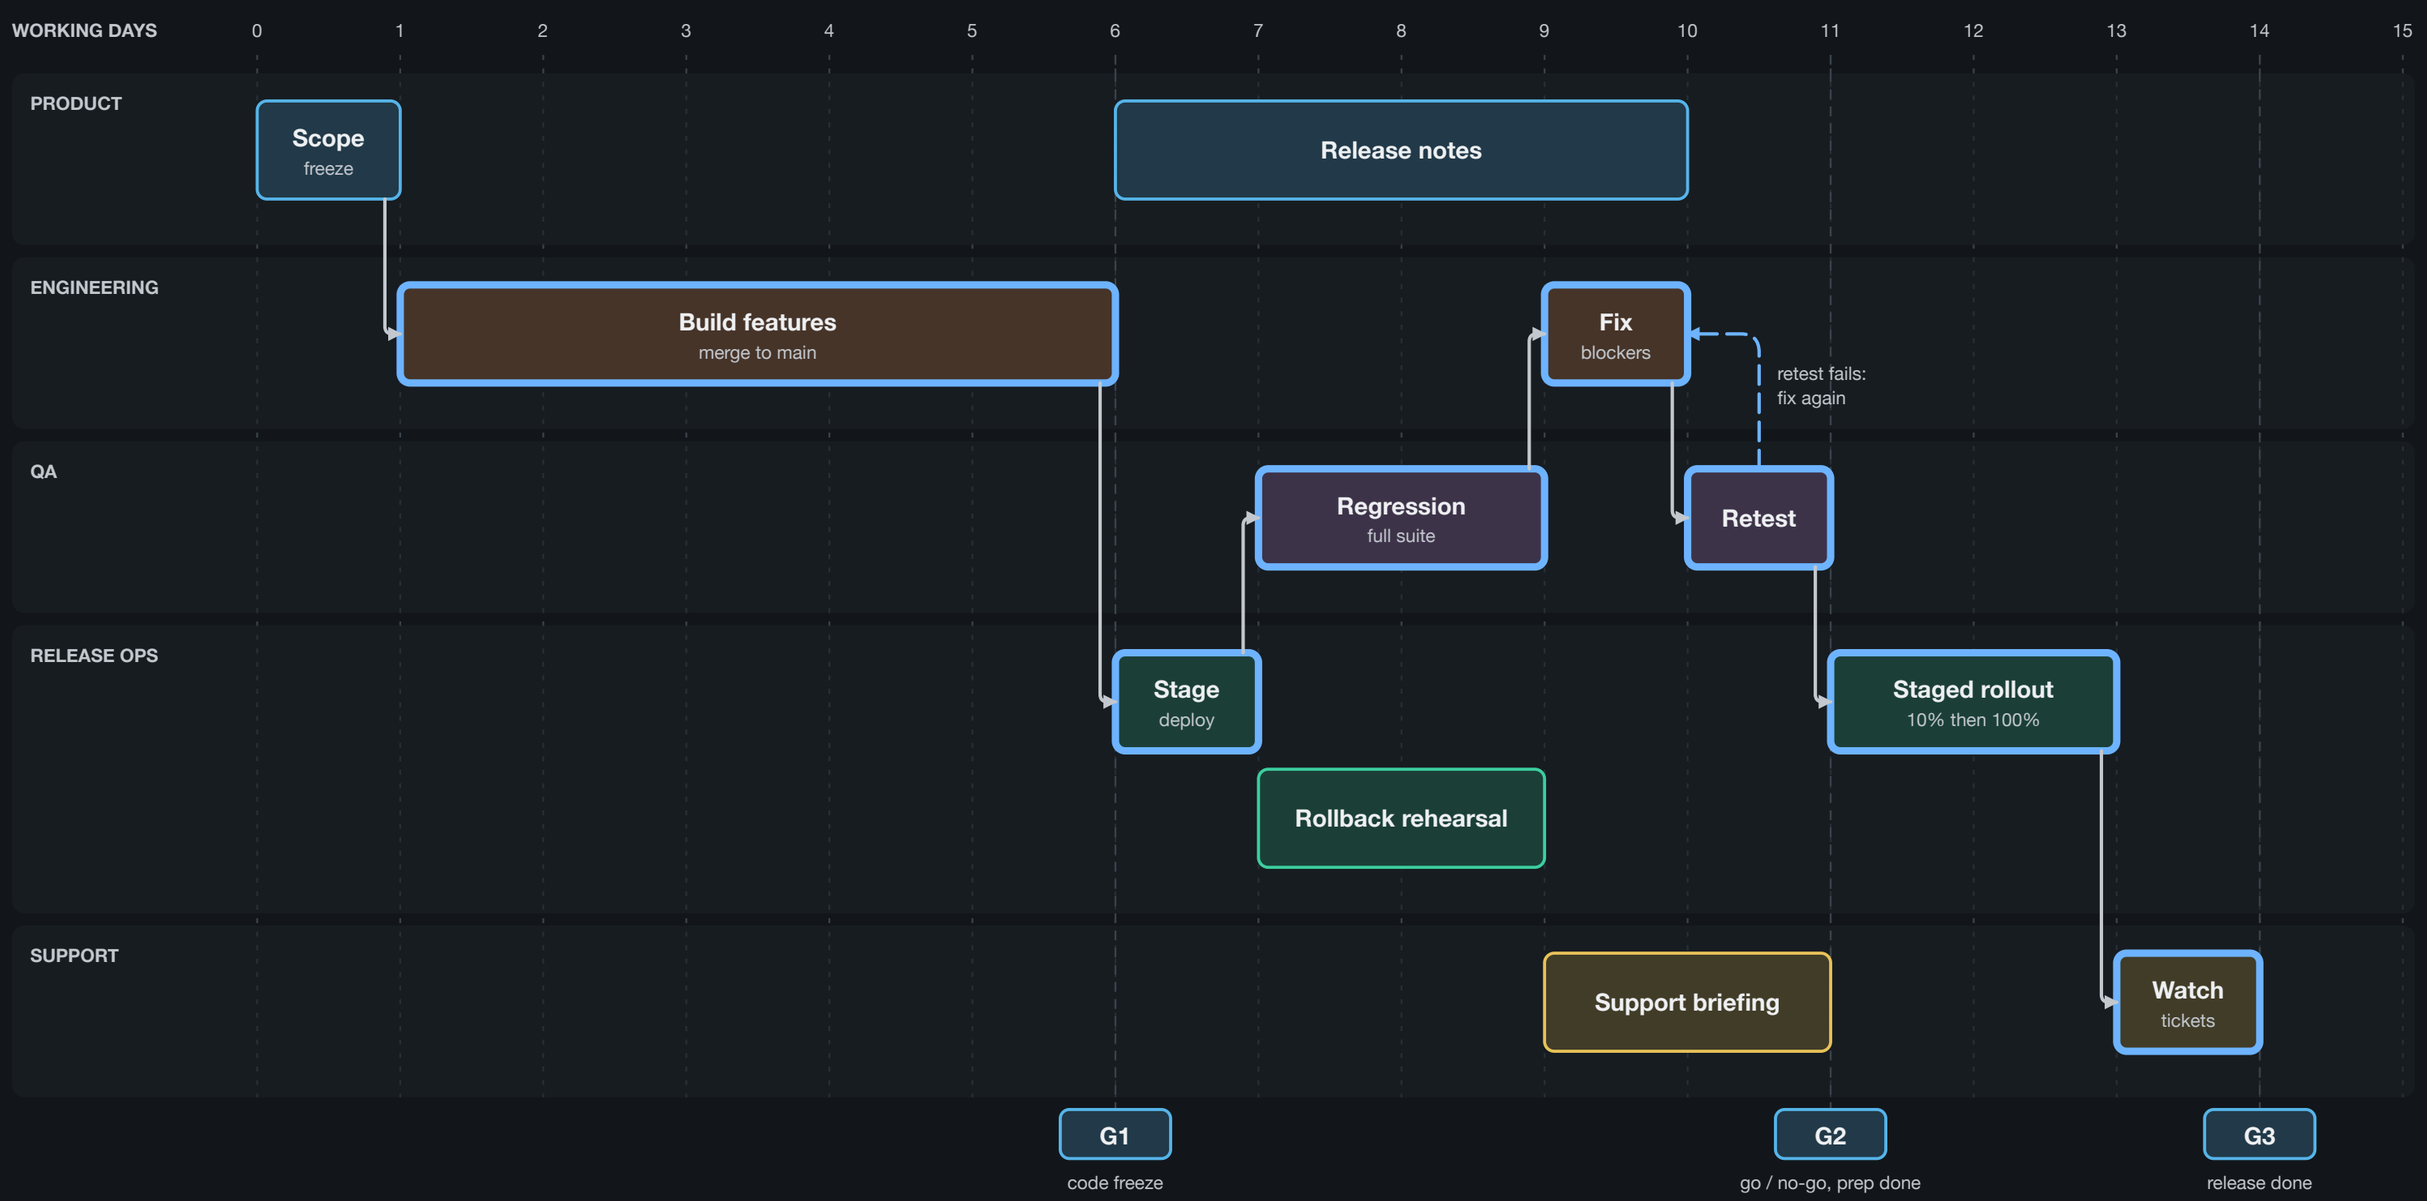

LEGEND lane = owner, bar length = days to scale, accent outline = critical path (longest chain), dashed line = rework, G = gate

Assumed: all durations describe a two-week cadence, not a measured team. **Decided:** three gates, G1 code freeze, G2 go / no-go, G3 done. **Open:** who calls G2?

Example page for the one-page-visual-design skill
